


# Works Program October 2017

ID	Task Name	Duration	Start	Finish	06 Aug '17							13 Aug '17							20 Aug '17							27 Aug '17							03 Sep '17							10 Sep '17						
					S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S
1	Eurella IS Project - Construction	86 days	Sat 01-07-17	Thu 26-10-17																																										
2	Sealing Works	2 days	Tue 10-10-17	Wed 11-10-17																																										
3	MR433 Maintenance Grading	73 days	Sat 01-07-17	Thu 09-11-17																																										
4	MR68C Maintenance Grading	27 days	Sat 01-07-17	Tue 08-08-17																																										
5	SR10 Maintenance Grading	25 days	Wed 09-08-17	Sun 10-09-17																																										
6	Porters Crossing - Construction	16 days	Mon 11-09-17	Wed 04-10-17																																										
7	Sealing Works	1 day	Mon 09-10-17	Mon 09-10-17																																										
8	SR9 Maintenance Grading	6 days	Thu 05-10-17	Tue 10-10-17																																										
9	SR5 Maintenance Grading	5 days	Wed 11-10-17	Thu 19-10-17																																										
10	SR6 Maintenance Grading	7 days	Fri 20-10-17	Thu 26-10-17																																										
11	SR14 Maintenance Grading	4 days	Tue 08-08-17	Sun 13-08-17																																										
12	SR35 Maintenance Grading	5 days	Mon 25-09-17	Tue 03-10-17																																										
13	Holding St - Construction	42 days	Tue 15-08-17	Wed 11-10-17																																										
14	Menindee Aerodrome Rd - Construction	2 days	Tue 17-10-17	Wed 18-10-17																																										
15	McGuinness Rd - Construction	2 days	Thu 19-10-17	Fri 20-10-17																																										
16	Menindee MR68B - Reconstruction	1 day	Sun 22-10-17	Sun 22-10-17																																										
17	Sealing Works	4 days	Mon 23-10-17	Thu 26-10-17																																										
18	Cobb Highway Maintenance Grading	30 days	Tue 17-10-17	Thu 23-11-17																																										
19	Barrier Highway Shoulder Grading	4 days	Mon 23-10-17	Thu 26-10-17																																										
20	State Highway Heavy Patching	10 days	Tue 31-10-17	Thu 09-11-17																																										
21	Sealing Works	3 days	Thu 02-11-17	Thu 09-11-17																																										
22	State Highway Reseals	4 days	Tue 14-11-17	Fri 17-11-17																																										

Project: Works Program October 2017  
Date: Mon 16-10-17

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

# Works Program October 2017

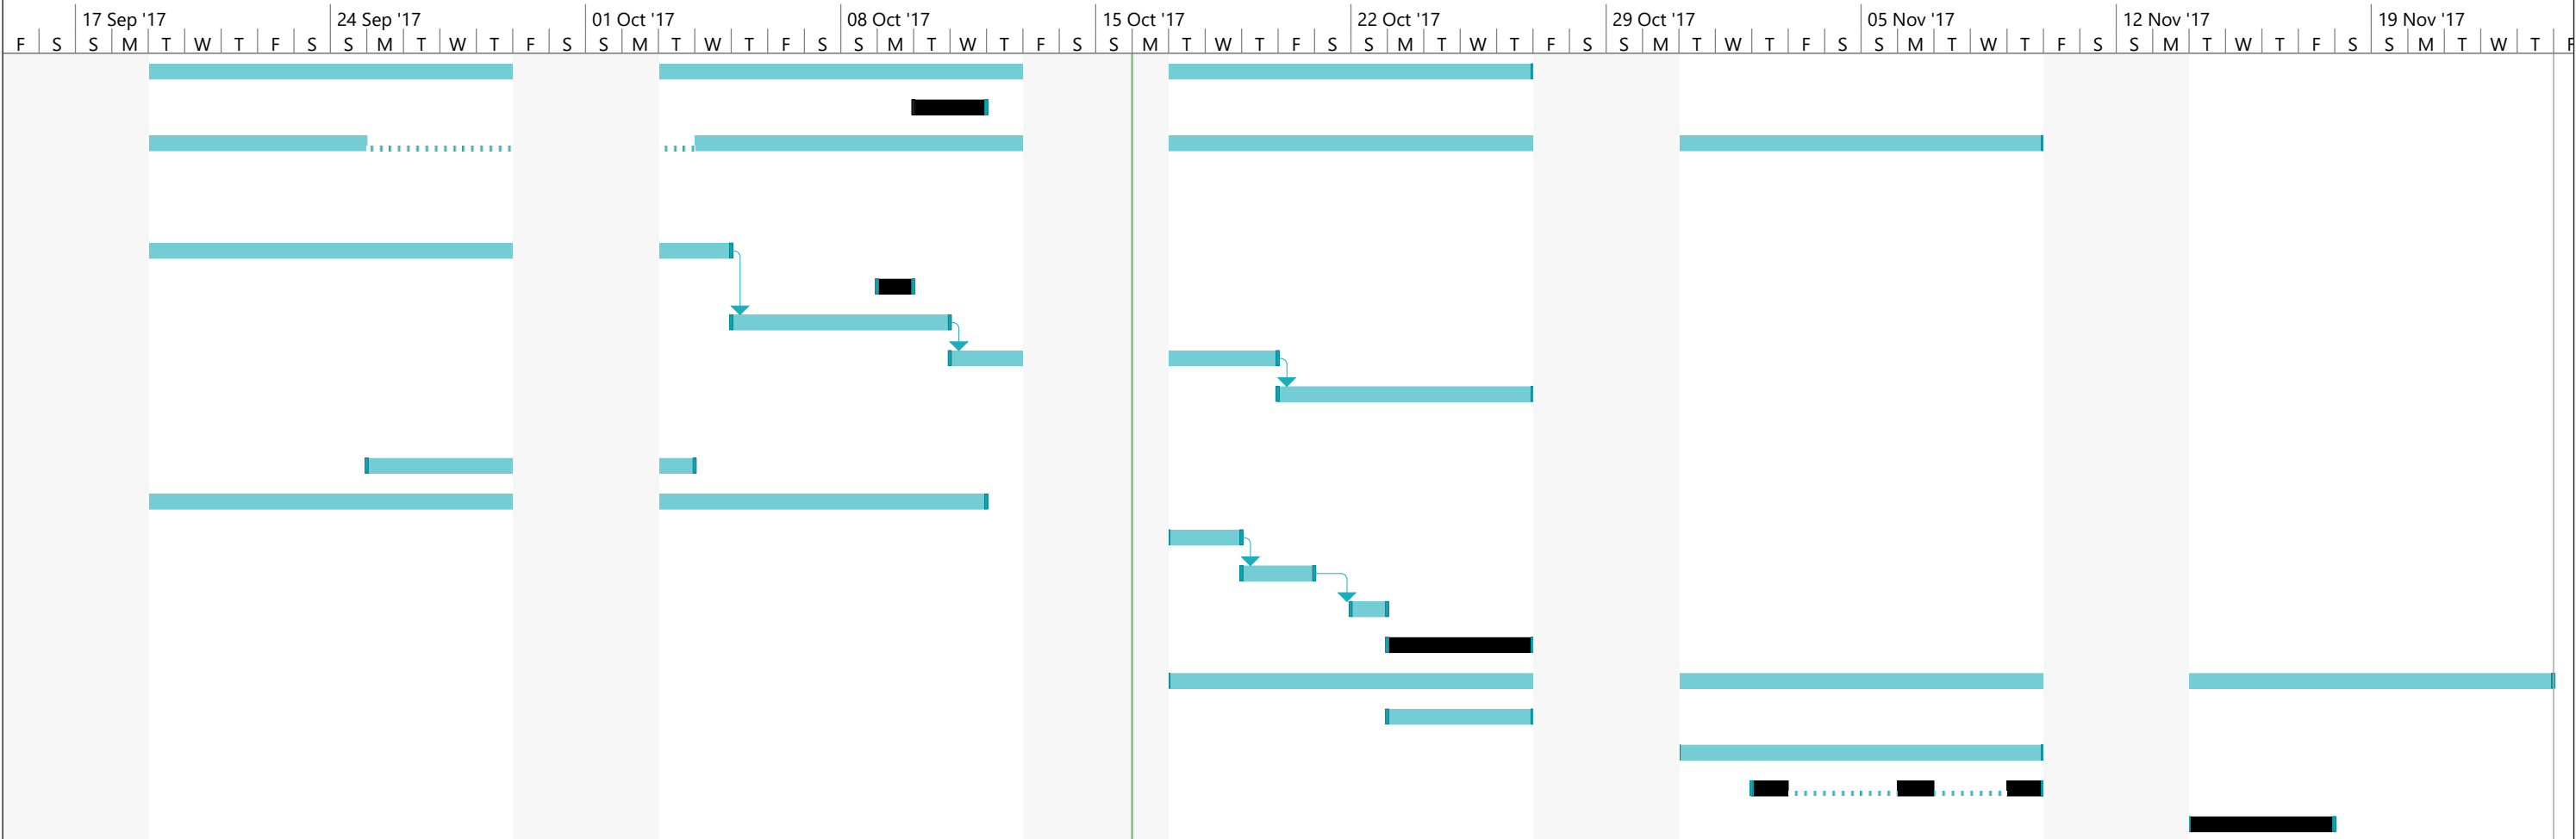

Project: Works Program Octobe  
Date: Mon 16-10-17

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			
